



[별첨1] 측정 위치도(측정 장소)

한국유에스지보랄(주) 성형동 복포장 및 폐기물장쪽 외벽 석면해체제거작업

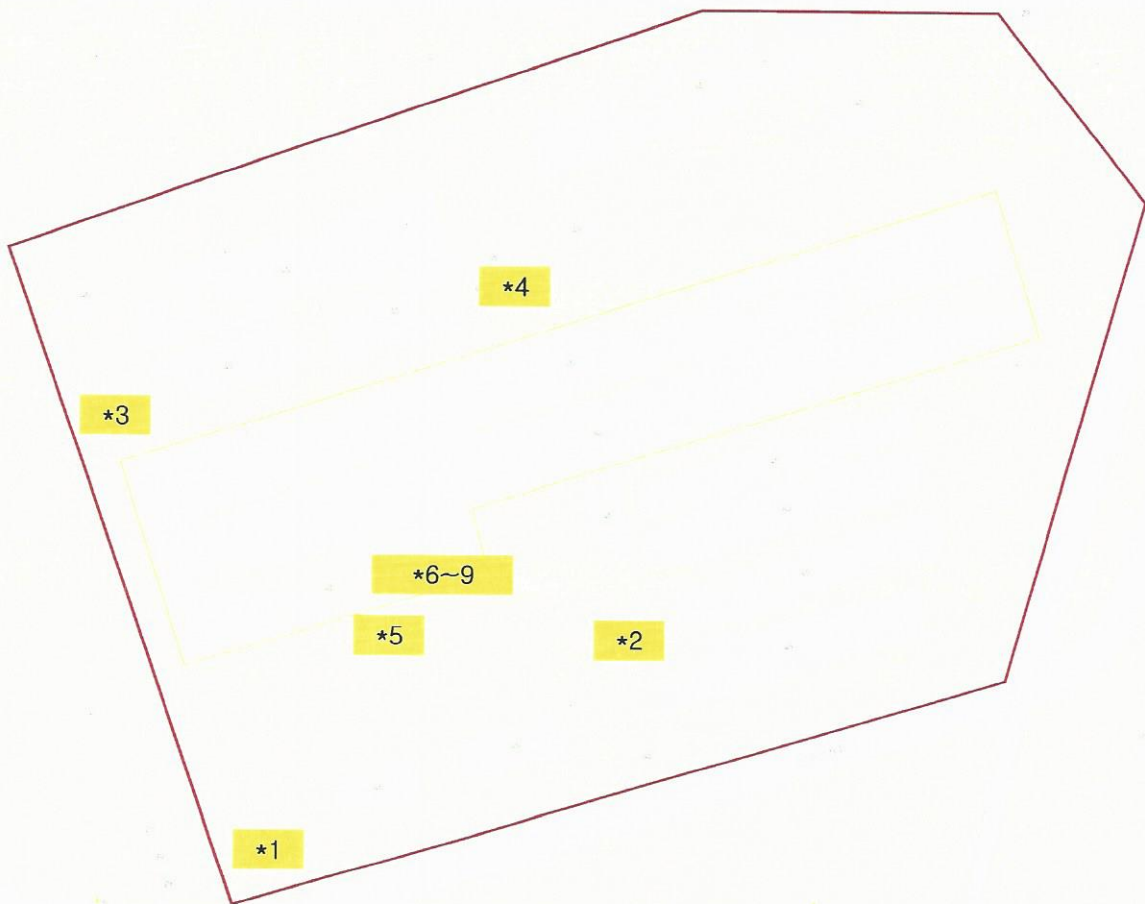

범례	*NO	
	시료채취	부지경계선

[별첨2] 측정 결과

측정위치	측정시간(분)	유량 (ℓ/min)	측정농도 [기준: 0.01개/㎤]	초과여부
*1 부지경계선1	10:23 ~ 14:23	10.00	불검출[검출한계 0.002미만]	미만
*2 부지경계선2	10:25 ~ 14:25	10.00	불검출[검출한계 0.002미만]	미만
*3 부지경계선3	10:29 ~ 14:29	10.00	불검출[검출한계 0.002미만]	미만
*4 부지경계선4	10:32 ~ 14:32	10.00	불검출[검출한계 0.002미만]	미만
*5 위생설비입구	10:37 ~ 11:17	10.00	불검출[검출한계 0.002미만]	미만
*6 작업장주변1	10:37 ~ 12:37	10.00	불검출[검출한계 0.002미만]	미만
*7 폐기물반출구1	10:44 ~ 11:24	10.00	0.003	미만
*8 작업장주변2	13:33 ~ 15:33	10.00	불검출[검출한계 0.002미만]	미만
*9 폐기물반출구2	13:37 ~ 14:17	10.00	0.003	미만

비고

[별첨3] 측정 사진

사 진			
			
*1. 부지경계선1	*2. 부지경계선2	*3. 부지경계선3	*4. 부지경계선4
			
*5. 위생설비입구	*6. 작업장주변1	*7. 폐기물반출구1	*8. 작업장주변2
			
*9. 폐기물반출구2	-	-	-
